

Work Order ID 140138

Thursday, December 17, 2015 3:43:08 PM

140138

Page 1

Item ID: D3065-5 Accept ***N900040100*** Setup Start ***NS1***
 Revision ID: Stop ***NS2***
 Item Name: Step Leg
 Start Date: 12/17/2015 Start Qty: 40.00 ***40*** Cust Item ID:
 Required Date: 12/17/2015 Req'd Qty: 40.00 ***40*** Customer:
 Reference:

Approvals: Process Plan: MLJ Date: DEC 23 2015 Tooling: _____ Date: _____
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____
 Run Start ***NR1***
 Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D3065	Rev B

100	FLOW WATER JET	0.00							
100									
Waterjet	Memo	0.03							
FLOW CNC Waterjet	1-Cut as per Dwg								
	Dwg Rev: <u>B</u>								
	Prog Rev: <u>B</u>								
	2-Deburr if necessary								

110	QC2- Inspect parts off machine FAI/FAIB	0.00							
110									
QC	Memo	0.01							
Quality Control									

(40) _____ PC 16/01/25

(40) _____ PC 16/01/25

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					

Root Cause			FAULT CATEGORY					
Environment ☐		No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐		
Design ☐		Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐		
Doc/Data ☐		Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐		
Equip/Tooling ☐		Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐		
Handling/Pre ☐		Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐		
Material ☐		Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐		
Internal Transport ☐		Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐		
Tribal Knowledge ☐		Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐		
LOA ☐		Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐		
Substation ☐		Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐		
Past Expiry Date ☐		Manufacturing Process ☐	OTHER : _____					
Misidentified ☐		Past Due ☐						

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
Root Cause		FAULT CATEGORY							
Environment ☐	☐ No Re-verification	☐ Pressure/Forced	☐ Temperature/Cure	☐ Power Loss/Surge	☐ Positioned Wrong				
Design ☐	☐ Operator	☐ Bending	☐ Set-up	☐ Folio/Program	☐ Outside Dimensions				
Doc/Data ☐	☐ Offset/Setup	☐ Centre Not Concentric	☐ BOM/Route	☐ Grain	☐ Over/Under tolerance				
Equip/Tooling ☐	☐ Supplier	☐ Cracks	☐ Broken/Damage/Defect	☐ Weld	☐ Part Incorrect				
Handling/Pre ☐	☐ Training	☐ Crimp/Kink/Ripple/Wave	☐ Inspection Incomplete/Unqualified	☐ Wrong Stock Pulled	☐ Part Lost/Missing				
Material ☐	☐ Use for Testing	☐ Cuffs	☐ Contamination	☐ Out of Sequence	☐ Part Moved				
Internal Transport ☐	☐ Poor Information	☐ Crushing	☐ Countersink	☐ Off-set	☐ Drawing				
Tribal Knowledge ☐	☐ Rushing	☐ Heat Treat	☐ Cut Too Short	☐ Mislabeled	☐ Finish				
LOA ☐	☐ Product Improvement	☐ Wave/Twist in Tube	☐ Instructions Incomplete/Unclear	☐ Fit/Function	☐ Misread				
Substation ☐	☐ Process Improvement	☐ Marks/Chatter	☐ Drill Holes	☐ Misaligned/off center	☐ Turning Sequence				
Past Expiry Date ☐	☐ Manufacturing Process	OTHER : _____							
Misidentified ☐	☐ Past Due								

Work Order ID 140138

140138

Page 3

Thursday, December 17, 2015 3:43:08 PM

Item ID: D3065-5

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: Step Leg

Start Date: 12/17/2015 Start Qty: 40.00

40

Cust Item ID:

Required Date: 12/17/2015 Req'd Qty: 40.00

40

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start

NR1

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop

NR2

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
150	Identify as per dwg & Stock Location: <u>GA</u>	0.00							
150									
Packaging	Memo	0.01							
Packaging	LOCATION : GA								
160	QC21- Final Inspection - Work Order Release	0.00							
160									
QC	Memo	0.07							
Quality Control									

MCS FEB 01 2016

MCS FEB 01 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : ☐					

Picklist Print

Thursday, December 17, 2015 3:43:08 PM

Page 1

Work Order ID: 140138

140138

Parent Item: D3065-5

D3065-5

Parent Item Name: Step Leg

Start Date: 12/17/2015

Required Date: 12/17/2015

Start Qty: 40.00

Required Qty: 40.00

Comments:

IPP: C02.11.01Incorporated D3066-1 IPPKJ/RF

IPP Rev:D Now on Water Jet 06-04-11 JLM

IPP Rev:E Now manufactured with 6061-T6 06-05-25 JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
M6061T6S.080		Purchased				100	sf	249.6000	0.825	34.73684			

M6061T6S 080

6061-T6 .080 Sheet

DL 16 / 01 / 2016

Location

Loc Qty

Loc Code

MAT020

249.6

m132772

57.6

m133587

96

m133828

96

32

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval	
Description Work Order Deviation				Disposition					

Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐			FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐					
			OTHER : ☐					

DART AEROSPACE LTD		Work Order:	140138
Description: Step Leg		Part Number:	D3065-5
Inspection Dwg: D3065	Rev: B	Page 1 of 1	

FIRST ARTICLE INSPECTION CHECKLIST

☒ First Article ☐ Prototype

Drawing Dimension	Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
16.458	+/-0.010	16.458	/		Viper-02	
15.750	+/-0.005	15.750	/		Viper-01	
2.250	+/-0.005	2.251	/		Tape	
3.460	+/-0.005	3.457	/			
0.865	+/-0.005	.865	/			
6.020	+/-0.005	6.022	/			
1.205	+/-0.005	1.204	/			
3.484	+/-0.005	3.485	/			
0.871	+/-0.005	.871	/			
8.325	+/-0.010	8.327	/			
0.551	+/-0.010	.549	/			
0.213	+0.005/-0.000	.212	/			
Ø0.128	+0.005/-0.000	Ø.127	✓			

Measured by:	de	Audited by:	DAS 38	Prototype Approval:	N/A
Date:	16/01/25	Date:	9-69 JAN 27 2016	Date:	N/A


Rev	Date	Change	Revised by	Approved
A	03.09.22	New Issue P/O D3065-041	KJ/RF	
B	04.06.15	Added Ø0.128 dimension	KJ/JLM	
C	06.06.23	Dwg Rev. changed	KJ/JLM	



DESIGN <i>CP</i>	DRAWN BY <i>CB</i>	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED <i>PH</i>	APPROVED <i>[Signature]</i>	DRAWING NO. D3065	REV. B SHEET 1 OF 5
DATE 06.05.23		TITLE STEP LEG ASSEMBLY	SCALE 1:2
A	02.09.11	NEW ISSUE	
B	06.05.23	ADD 6061-T6 MATERIAL, ADD SLOTS TO D3065-5	

RELEASED

06.06.20 *[Signature]*

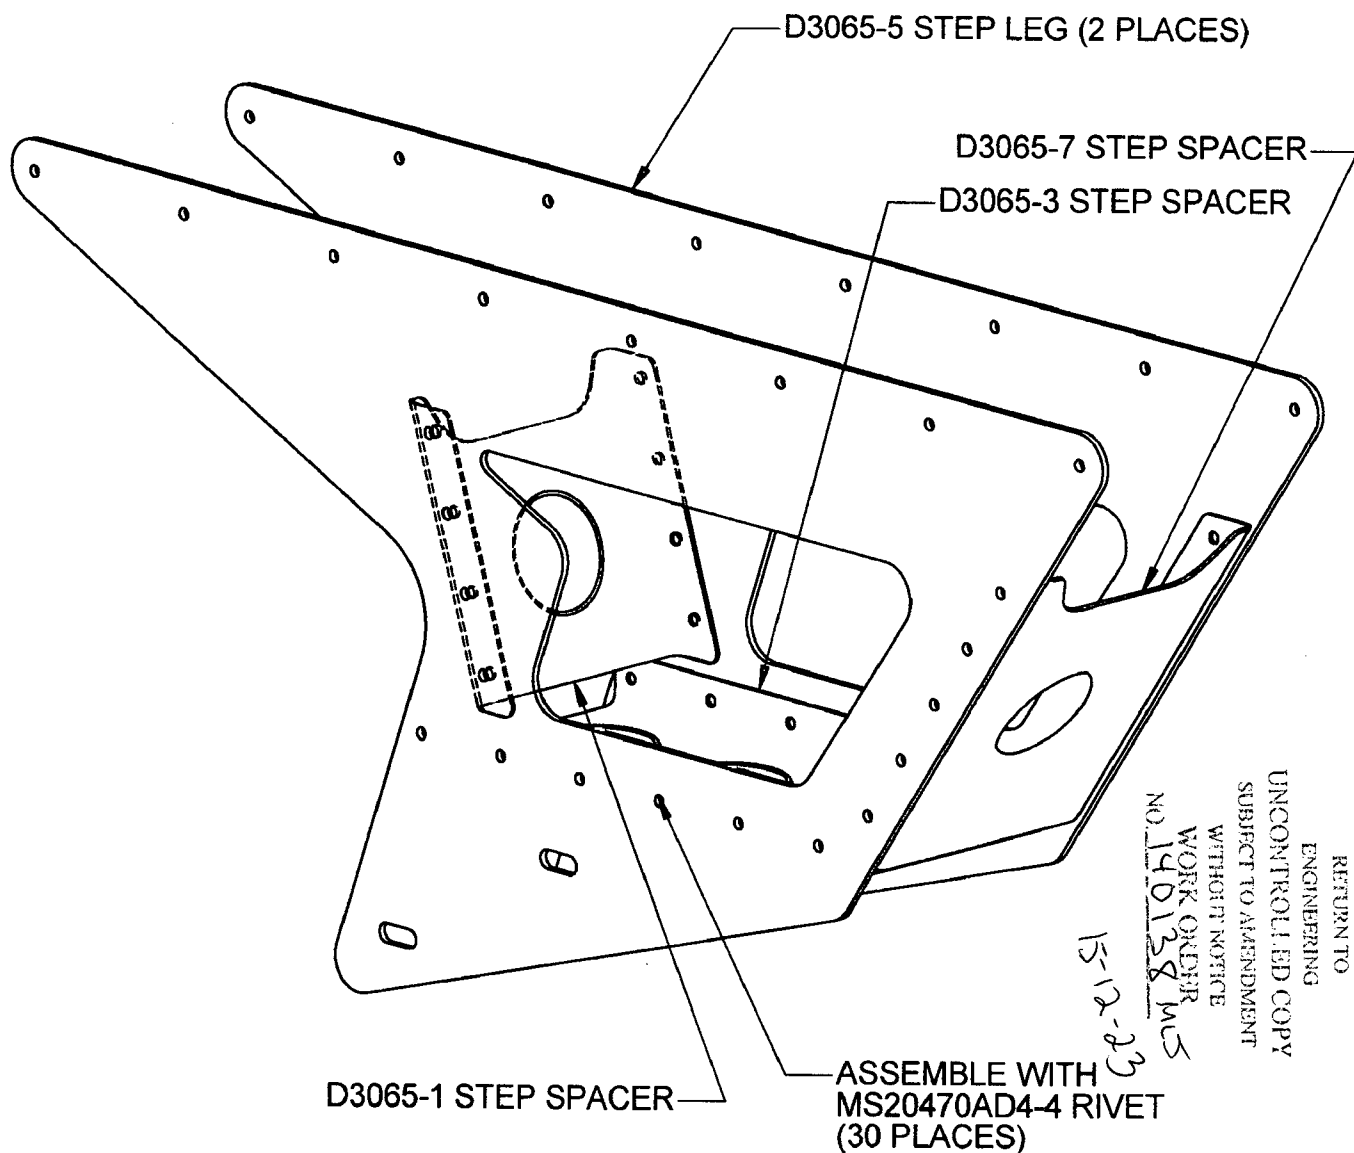



SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 140138 M5

D3065-041 STEP LEG ASSEMBLY

COPYRIGHT © 2002 BY DART AEROSPACE LTD.

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

DESIGN <i>CP</i>	DRAWN BY <i>CB</i>	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED <i>PH</i>	APPROVED <i>[Signature]</i>	DRAWING NO. D3065	REV. B SHEET 2 OF 5
DATE 06.05.23		TITLE STEP LEG ASSEMBLY	SCALE 1:1

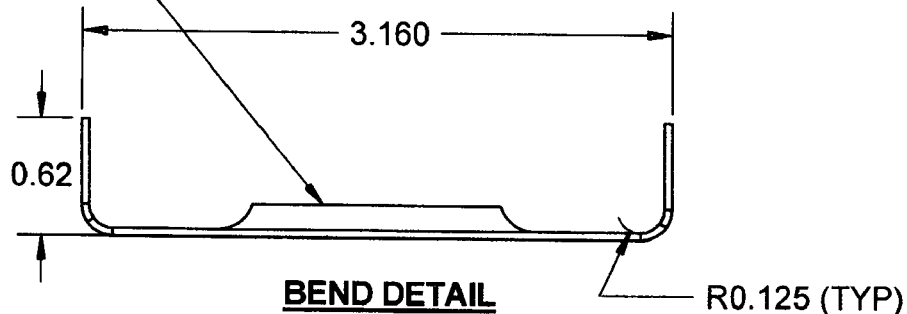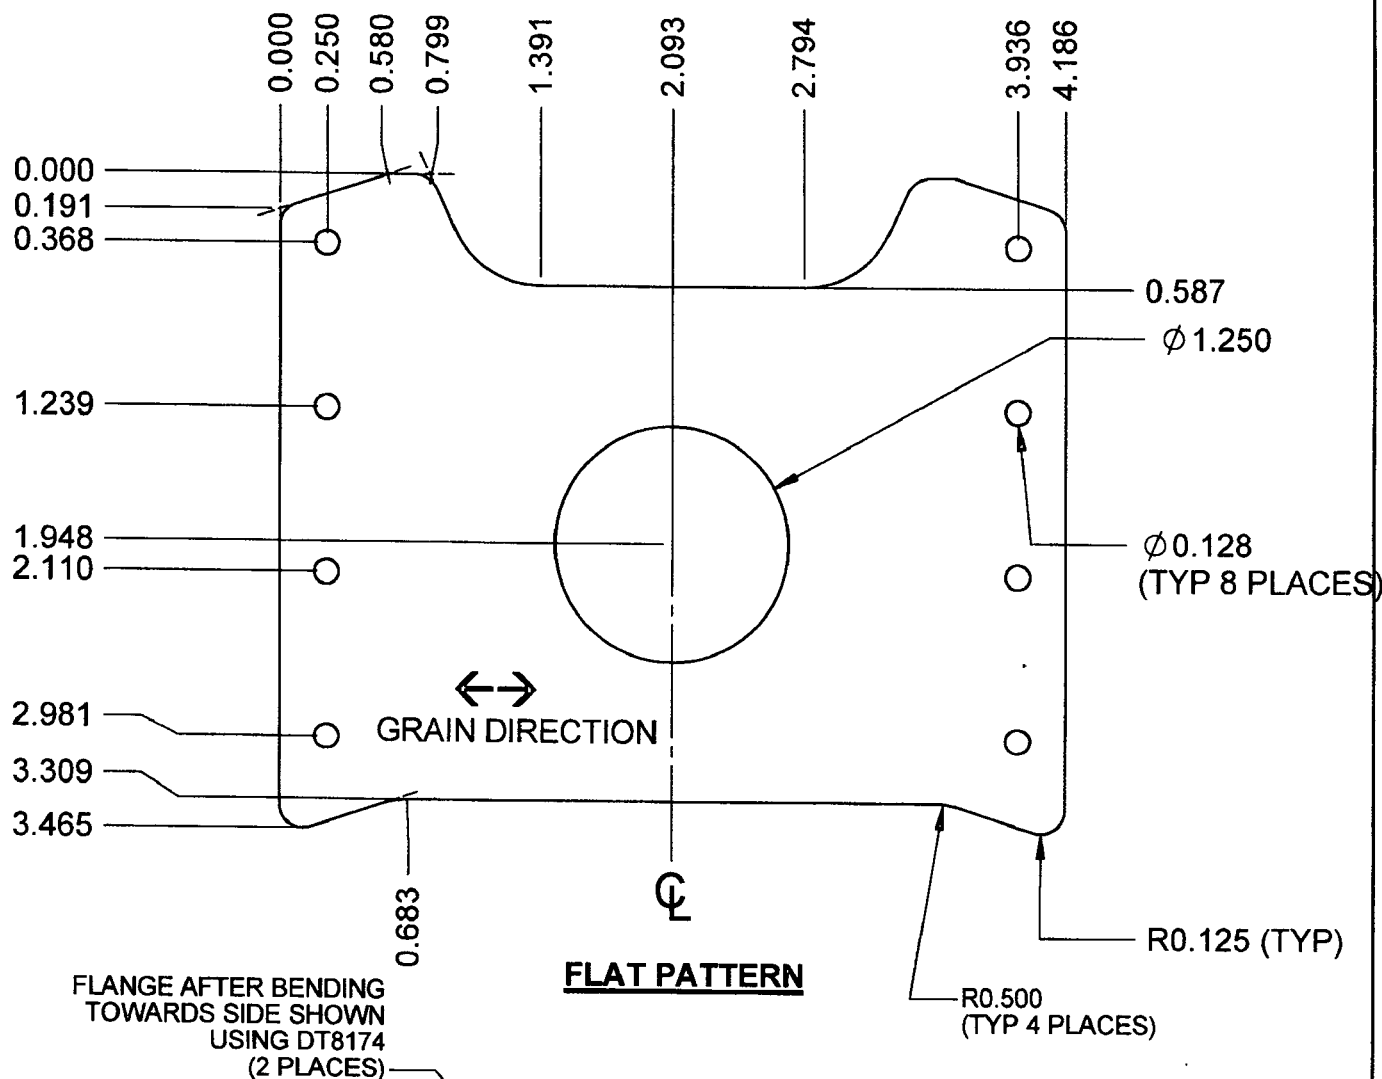

D3065-1 STEP SPACER


- 1) MATERIAL: 2024-T3 (QQ-A-250/4) 0.040 THICK (REF DART SPEC. M2024T3S.040)
2) FINISH: ACID ETCH & ALODINE PER DART QSI 005 4.1
3) BREAK ALL SHARP EDGES 0.005 TO 0.010
4) PART IS SYMMETRIC ABOUT CENTERLINE
5) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED
6) ALL DIMENSIONS ARE IN INCHES

COPYRIGHT © 2002 BY DART AEROSPACE LTD.

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.



DESIGN <i>CP</i>	DRAWN BY <i>CB</i>	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED <i>PH</i>	APPROVED <i>[Signature]</i>	DRAWING NO. D3065	REV. B SHEET 3 OF 5
DATE 06.05.23	TITLE STEP LEG ASSEMBLY		
			SCALE 1:1

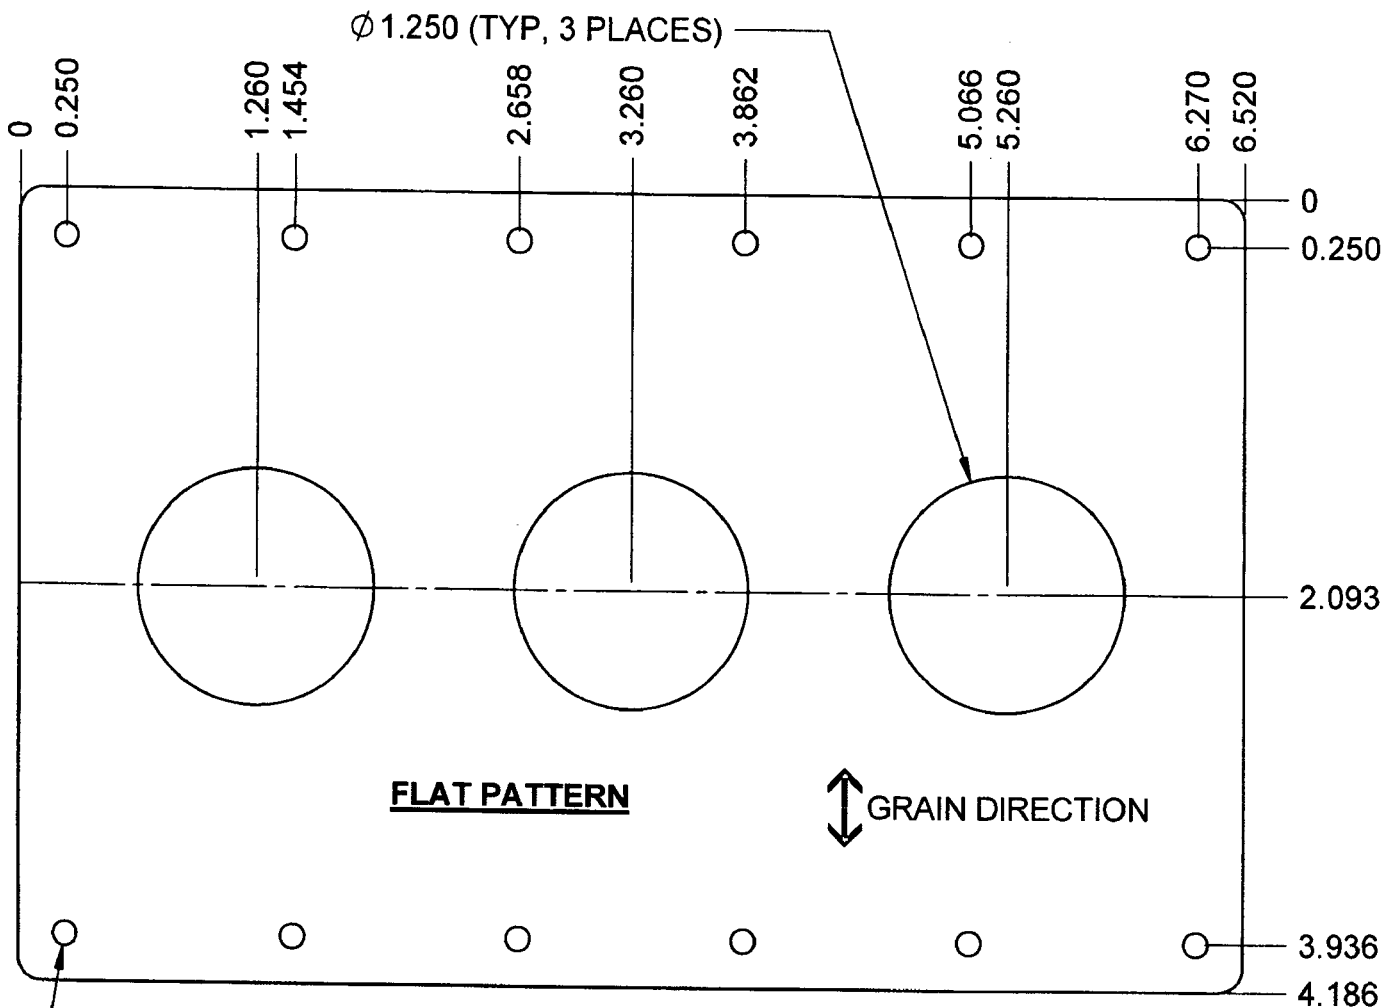


FLANGE AFTER TOWARDS SIDE
SHOWN USING DT8174 (3 PLACES)

Ø 0.129 (TYP, 12 PLACES)

RELEASED

06 Oct 20 *[Signature]*

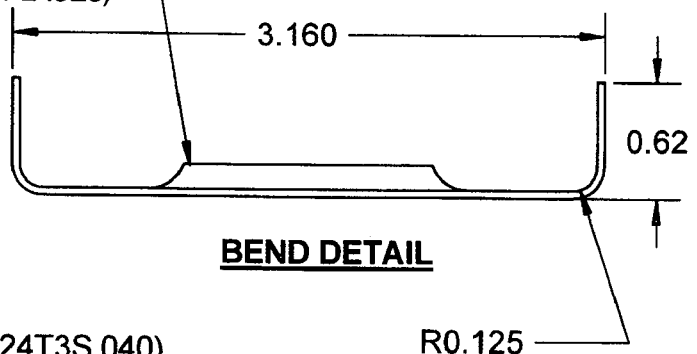

D3065-3 STEP SPACER


- 1) MATERIAL: 2024-T3 (QQ-A-250/4)
0.040 THICK (REF DART SPEC. M2024T3S.040)
- 2) FINISH: ACID ETCH & ALODINE PER DART QSI 005 4.1
- 3) PART IS SYMMETRIC ABOUT CENTERLINE
- 4) BREAK ALL SHARP EDGES 0.005 TO 0.010
- 5) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED
- 6) ALL DIMENSIONS ARE IN INCHES

COPYRIGHT © 2002 BY DART AEROSPACE LTD.

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.



DESIGN	DRAWN BY	DART AEROSPACE LTD	
		HAWKESBURY, ONTARIO, CANADA	
CHECKED	APPROVED	DRAWING NO.	REV. B
PH	JK	D3065	SHEET 4 OF 5
DATE	TITLE		SCALE
06.05.23	STEP LEG ASSEMBLY		1:3

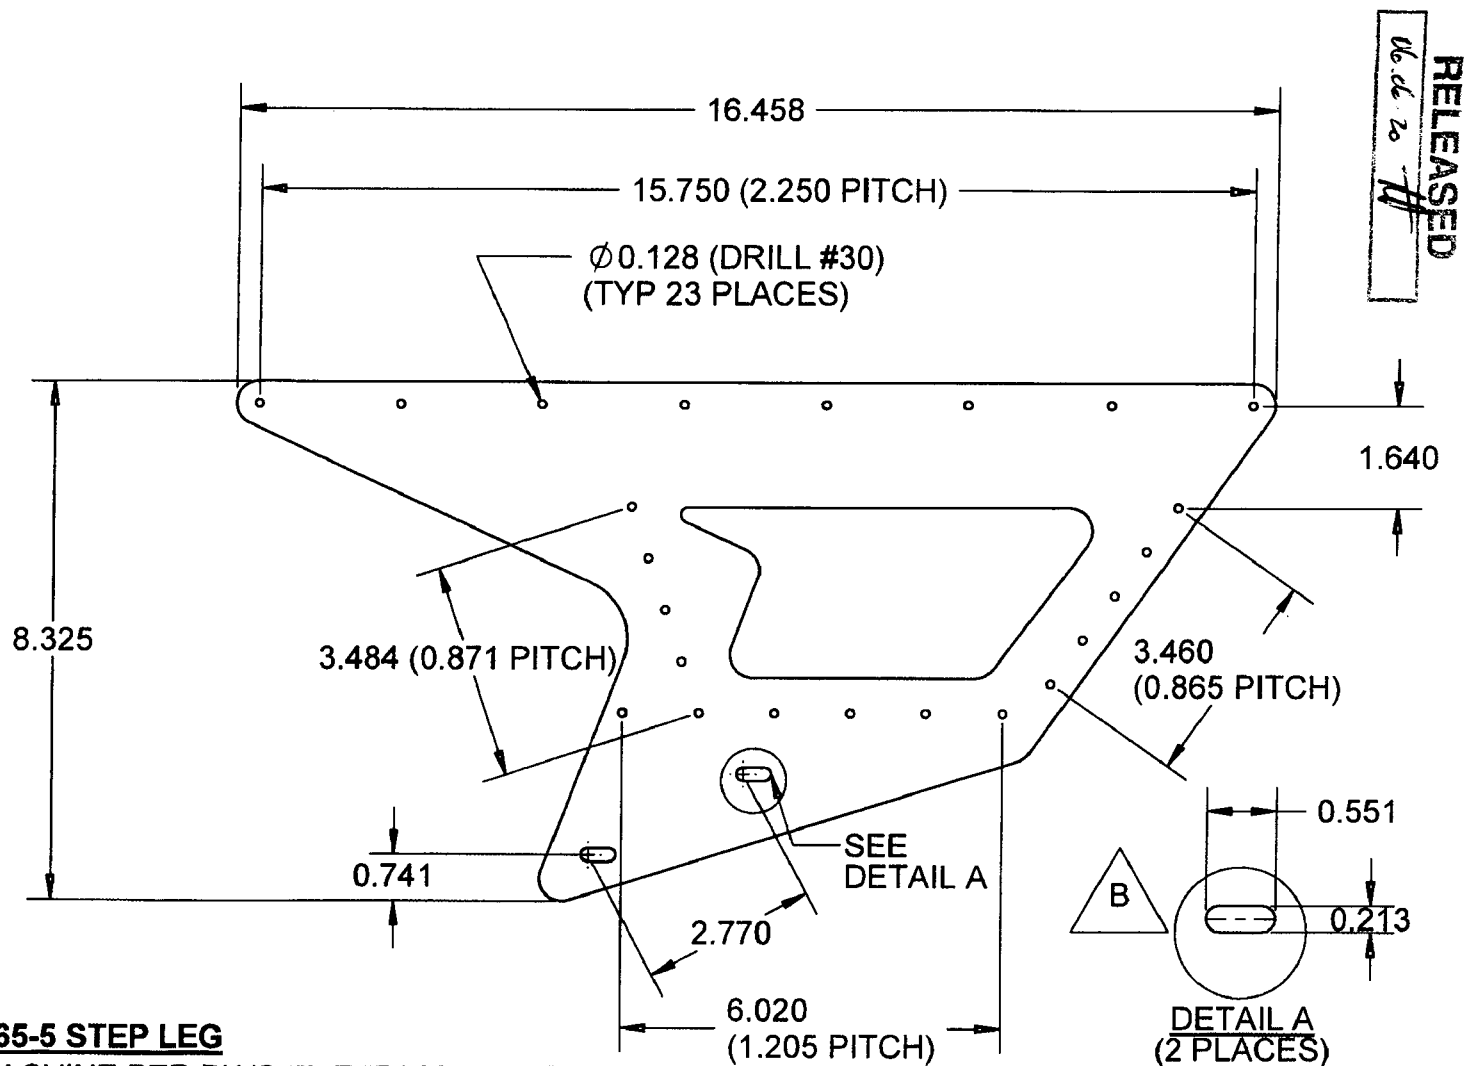


D3065-5 STEP LEG

- 1) MACHINE PER DWG FILE "D3065-5.SLDPRT"
2) MATERIAL: 6061-T6 (PER QQ-A-250/11 OR AMS 4025 OR AMS 4027) 0.080" THICK
(REF DART SPEC M6061T6S.080)
OR
5052-H32 (PER QQ-A-250/8 OR AMS 4016) 0.080 THICK (REF DART SPEC. M5052H32S.080)
3) FINISH: ACID ETCH & ALODINE PER DART QSI 005 4.1
4) BREAK ALL SHARP EDGES 0.005 TO 0.010
5) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED
6) ALL DIMENSIONS ARE IN INCHES



DESIGN <i>CP</i>	DRAWN BY <i>CB</i>	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED <i>PH</i>	APPROVED <i>[Signature]</i>	DRAWING NO. D3065	REV. B SHEET 5 OF 5
DATE 06.05.23	TITLE STEP LEG ASSEMBLY		SCALE 1:1

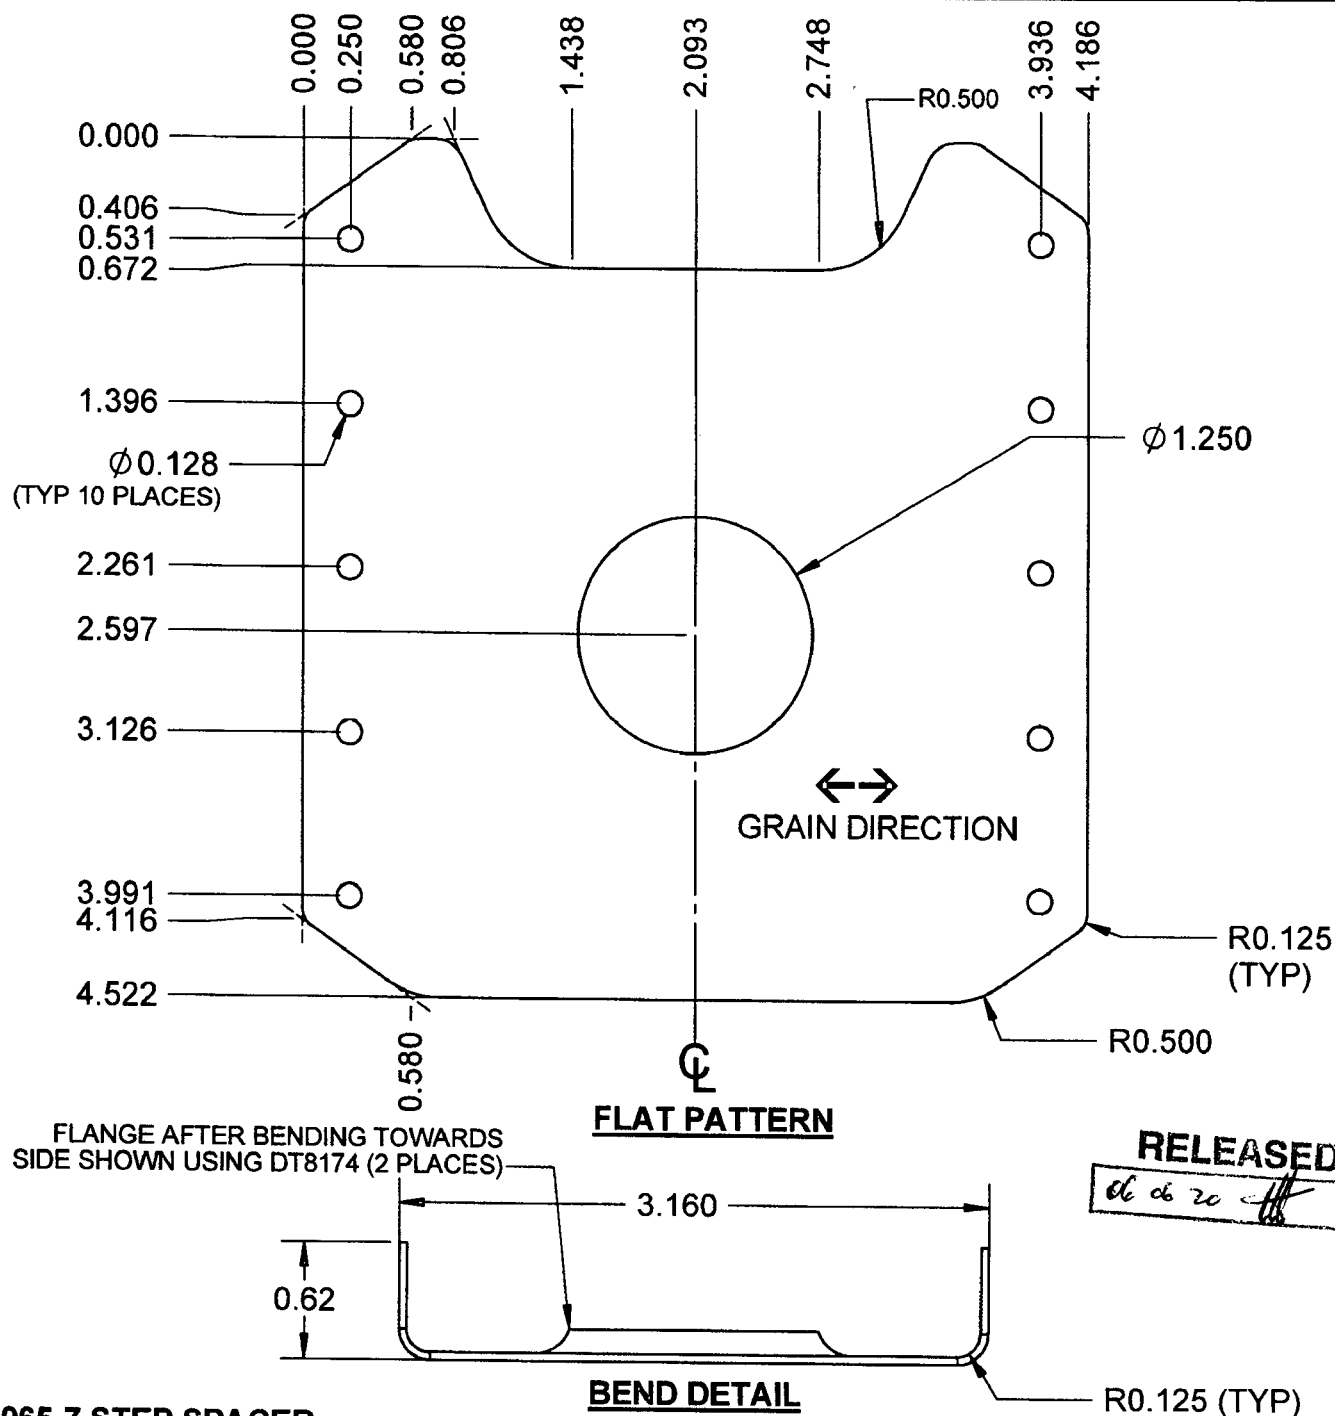

RELEASED

D3065-7 STEP SPACER

- 1) MATERIAL: 2024-T3 (PER QQ-A-250/4) 0.040 THICK (REF DART SPEC. M2024T3S.040)
- 2) FINISH: ACID ETCH & ALODINE PER DART QSI 005 4.1
- 3) PART IS SYMMETRIC ABOUT CENTERLINE
- 4) BREAK ALL SHARP EDGES 0.005 TO 0.010
- 5) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED
- 6) ALL DIMENSIONS ARE IN INCHES

COPYRIGHT © 2002 BY DART AEROSPACE LTD.

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.
